

# **Chautauqua Lake Campus Committee Meeting**

**August 15th, 2023**



# CHAUTAUQUA LAKE CAMPUS COMMITTEE MEMBERS

- Jessup Baker, Board Member, Parent, Community Member
- Ken Shearer, Board Member, Parent, Community Member
- John McKane, Buildings & Grounds, Community Member, Parent
- Burl Swanson, Community Member
- Tim Brunswick, Clerk of the Works
- Rachel Curtin, Secondary Principal, Ripley Alum
- Megan Lundgren, Elementary Principal
- Sarah Graham, K-12 Asst. Principal
- Derek Svenson, Director of Technology
- Jeff Angeletti, Building Operations, Support Services & Athletics Supervisor
- Jackson Graham, Business Executive
- Dr. Josh Liddell, Superintendent, Former AD & Principal
- Nick Raynor, Teacher & Parent
- Melanie Cannon, Parent, Coach, CL BOCES Service Provider, Chautauqua CSD Alum
- Jacob Mountain, Project Manager CPL
- Brady Morrison, Senior Architectural Designer CPL
- Brendan Kelleher, School Attorney
- Ken Rowe, Coach, Ripley Alum, Parent
- Logan Betts, Teacher, Parent, Chautauqua Lake CSD Alum
- Emily Dorman, Teacher, Coach, Parent
- Mike Rohlin, Teacher, Coach
- Bryan Bongiovanni, Dean of Students, Supervisor of Athletics

**Essential Question: Is everyones name depicted above and is this information accurate?**

# COMMITTEE ROLES & RESPONSIBILITIES



## CL Campus Committee

This committee is responsible for **identifying all areas where the nickname and or coinciding imagery appears and the process in which these areas are removed and/or modified.**

## CL Design Committee\*

They are responsible for **working with members of our professional learning community to identify and bring to the board approval for a new “nickname” and corresponding imagery.**

*\*Will be meeting late early September*

# Present Areas Identified by Committee with Thunderbird Logo



- FIELD TURF
- FRONT SIGN
- TENNIS COURTS PAINT
- WINDSCREENS
- INTERIOR PLAQUES
- STEM LAB PLAQUE
- MULTI-PURPOSE ROOM
- LGI ACOUSTICAL WALL PADS
- GYMNASIUM SCOREBOARDS
- LARGE HALLWAY STICKERS
- MISCELLANEOUS: NAVIGATOR, SCHOOL CALENDAR, CHARACTER TRAIT POSTERS, ETC.

**Question: Are we missing anything? Thanks to committee members who emailed us.**




# Athletic Complex/Field Turf



**Committee Decision: Remove the logo (Thunderbird far right D zone in pic above) and replace with pitching mounds and provide an area for baseball/softball practice.**

**Status: Change proposal has been received/approved for this work. Board of Education notified.**

# Athletic Complex/Field Turf

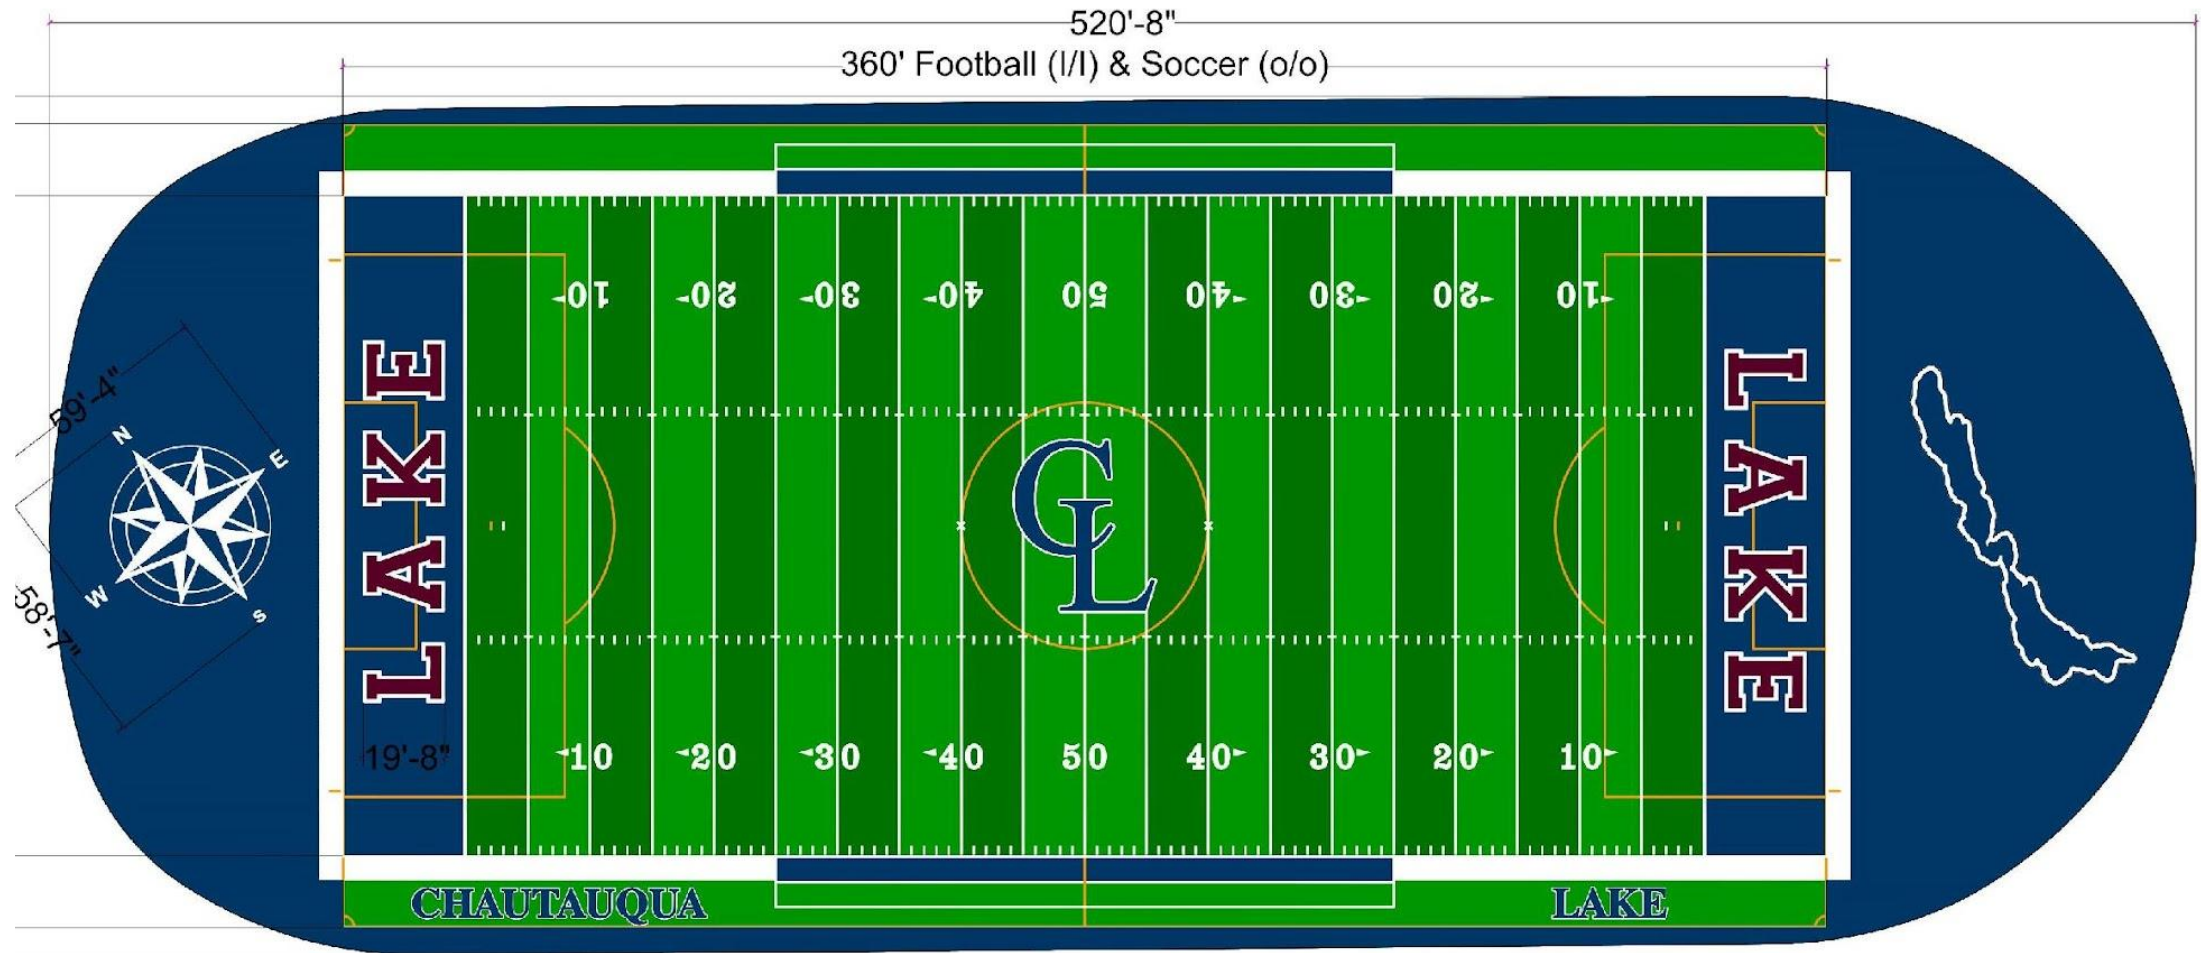

No compass or other logo replacement for Thunderbird  
Essential Question: Where do we put softball pitching mounds?



# FRONT SIGN



Discussion about funding implications if we wait or use something existing.

Group Consensus: Hold on changing, but push the other committee to make a design timely to try and use funding.

Will attempt to make this #1 priority once decision made on mascot. May not make capital project deadline....






FRONT SIGN




# TENNIS COURTS

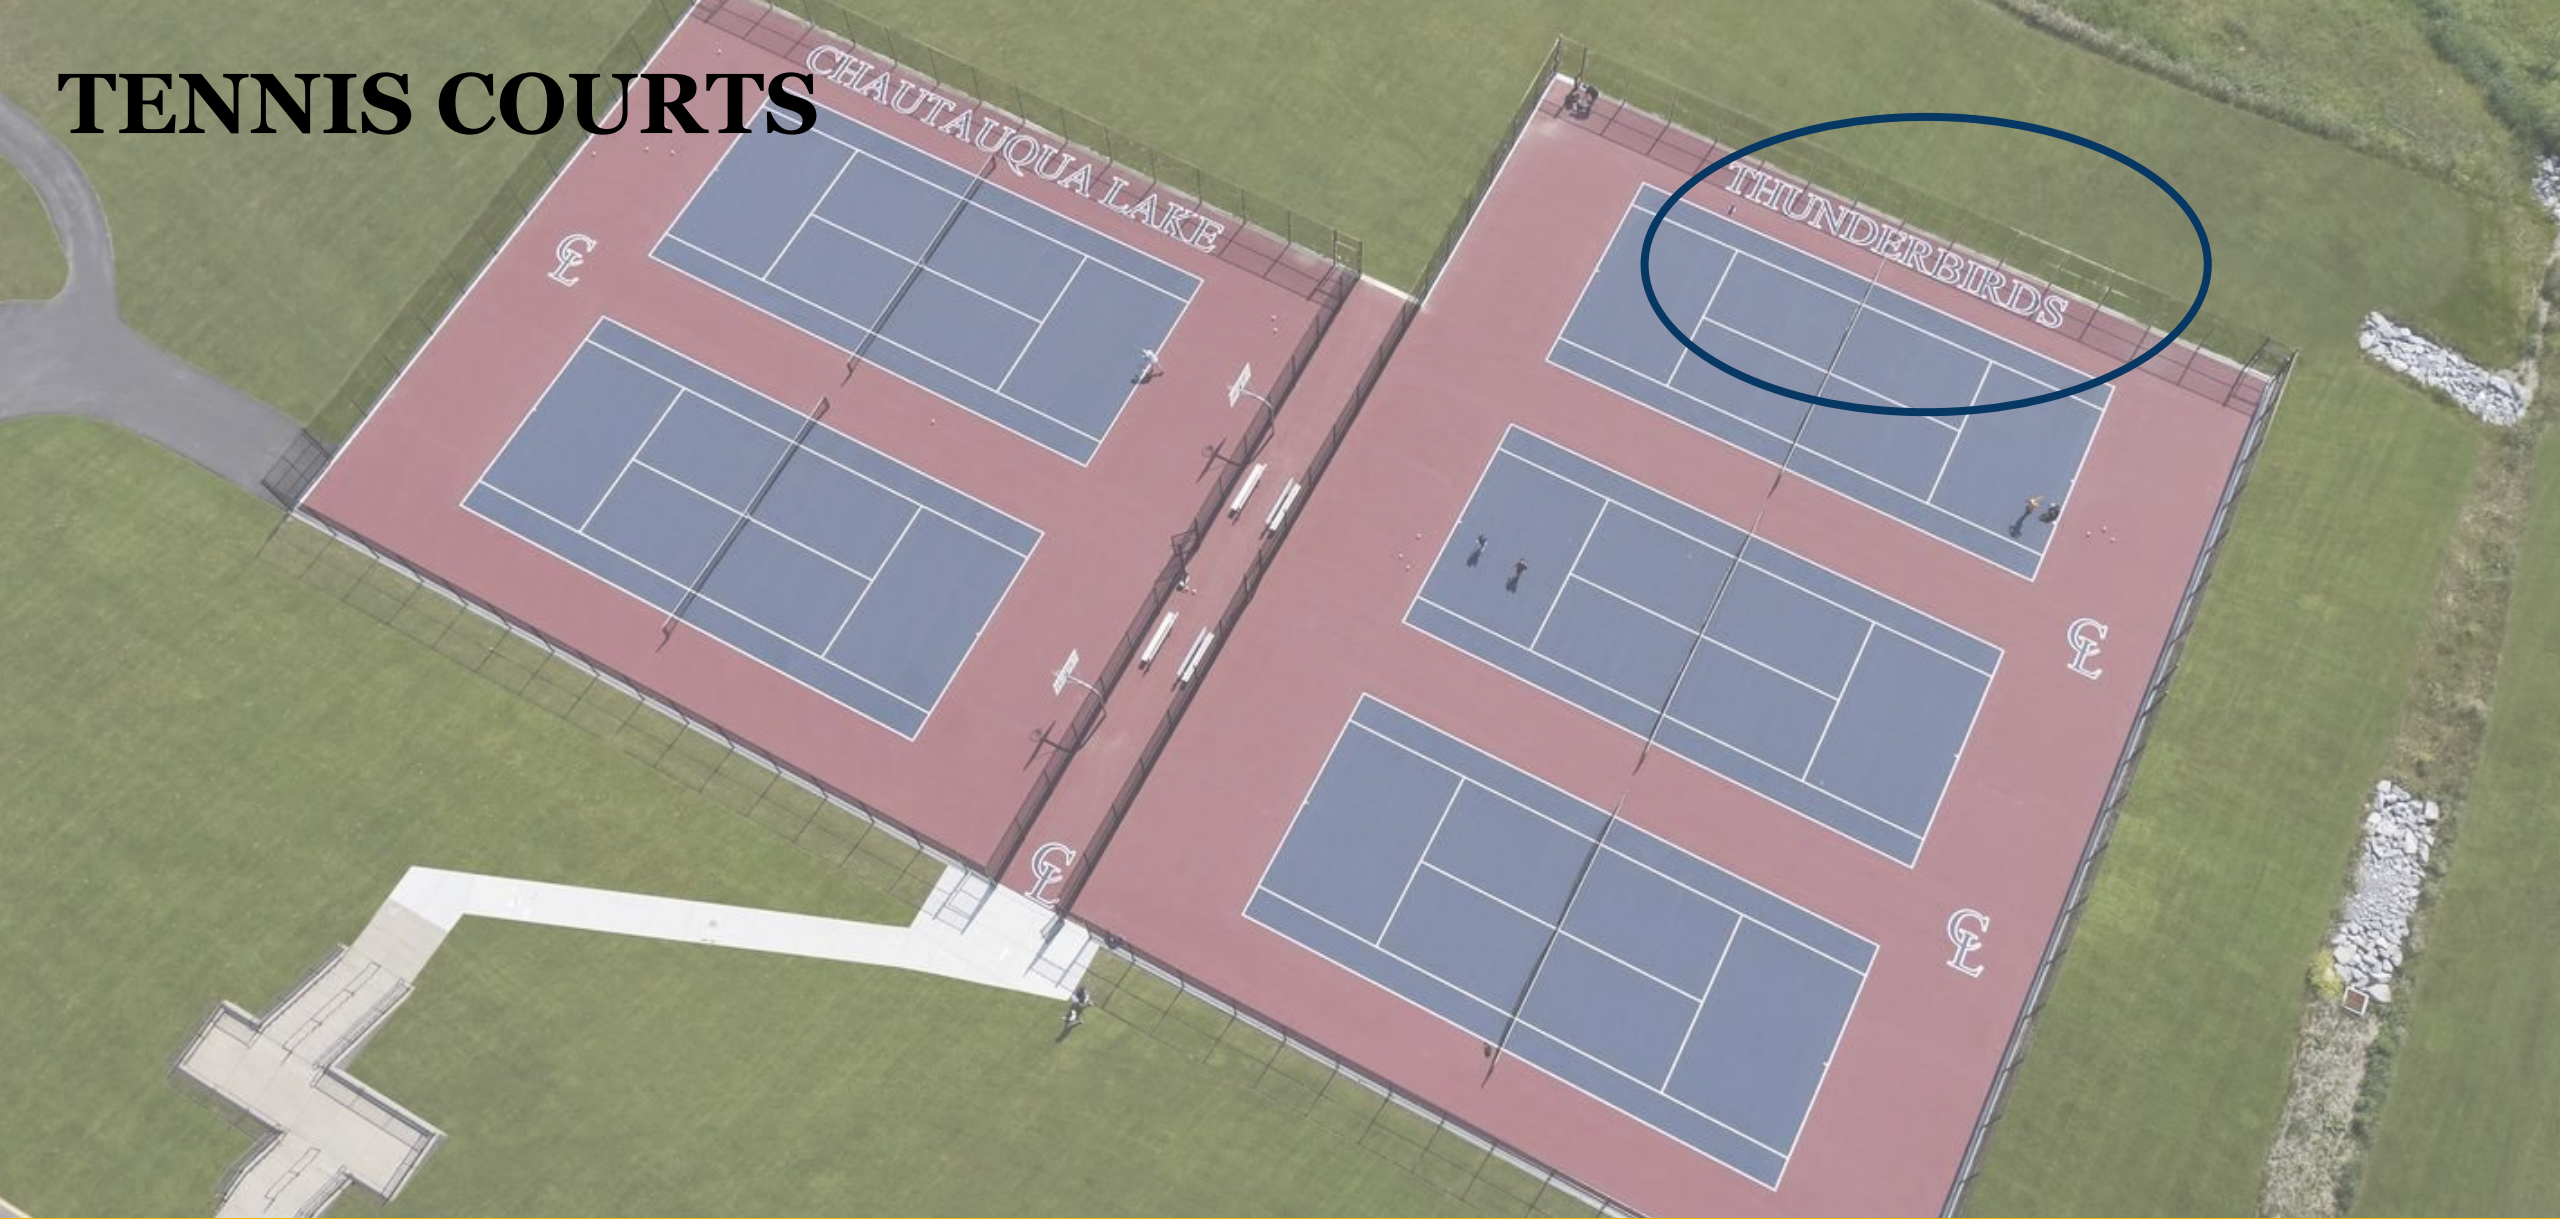

Status: The Thunderbirds verbiage will be removed and left blank. This work has been scheduled with the contractor.

# Windscreens

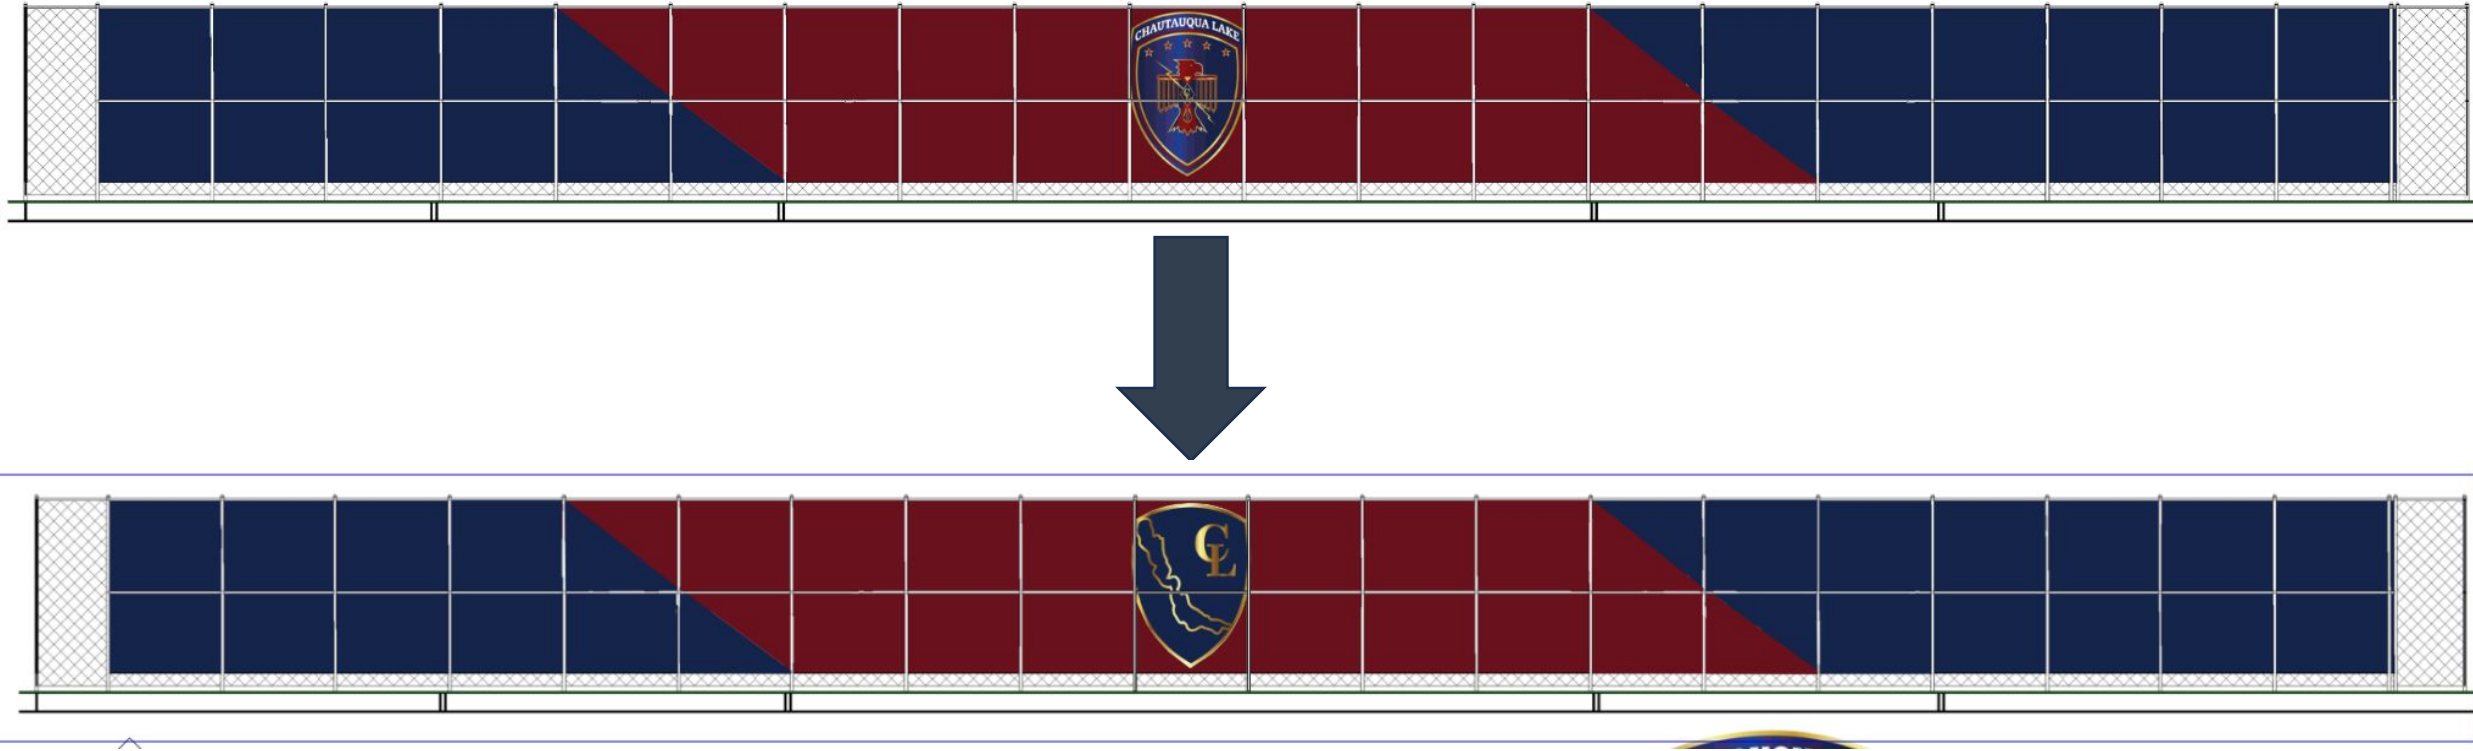


**Status: See change above. Is everyone okay with this change?**



# Vinyl Graphics



BEFORE

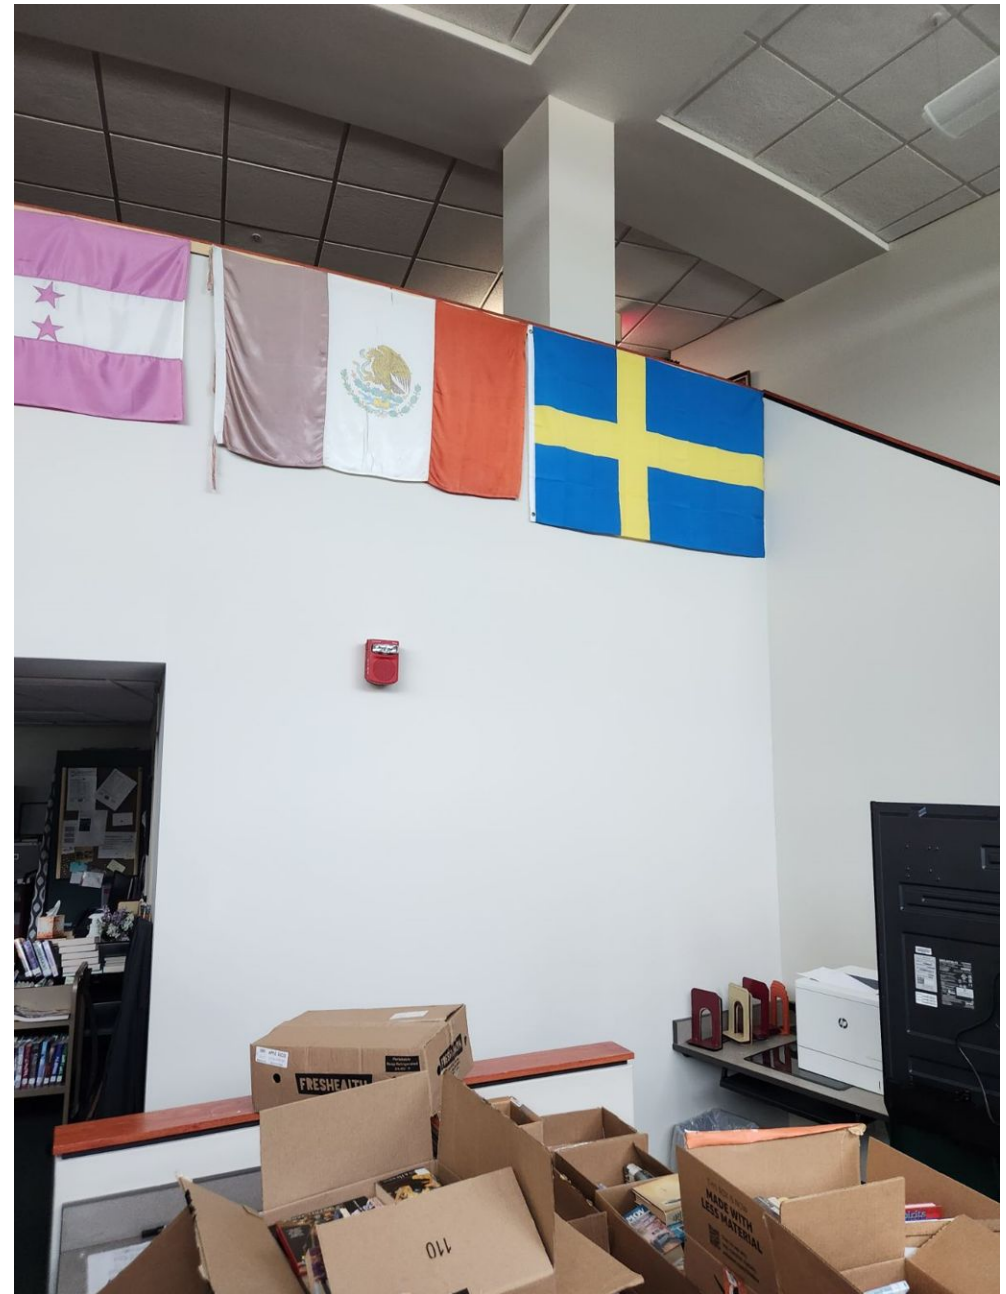


AFTER



# Vinyl Graphics



BEFORE

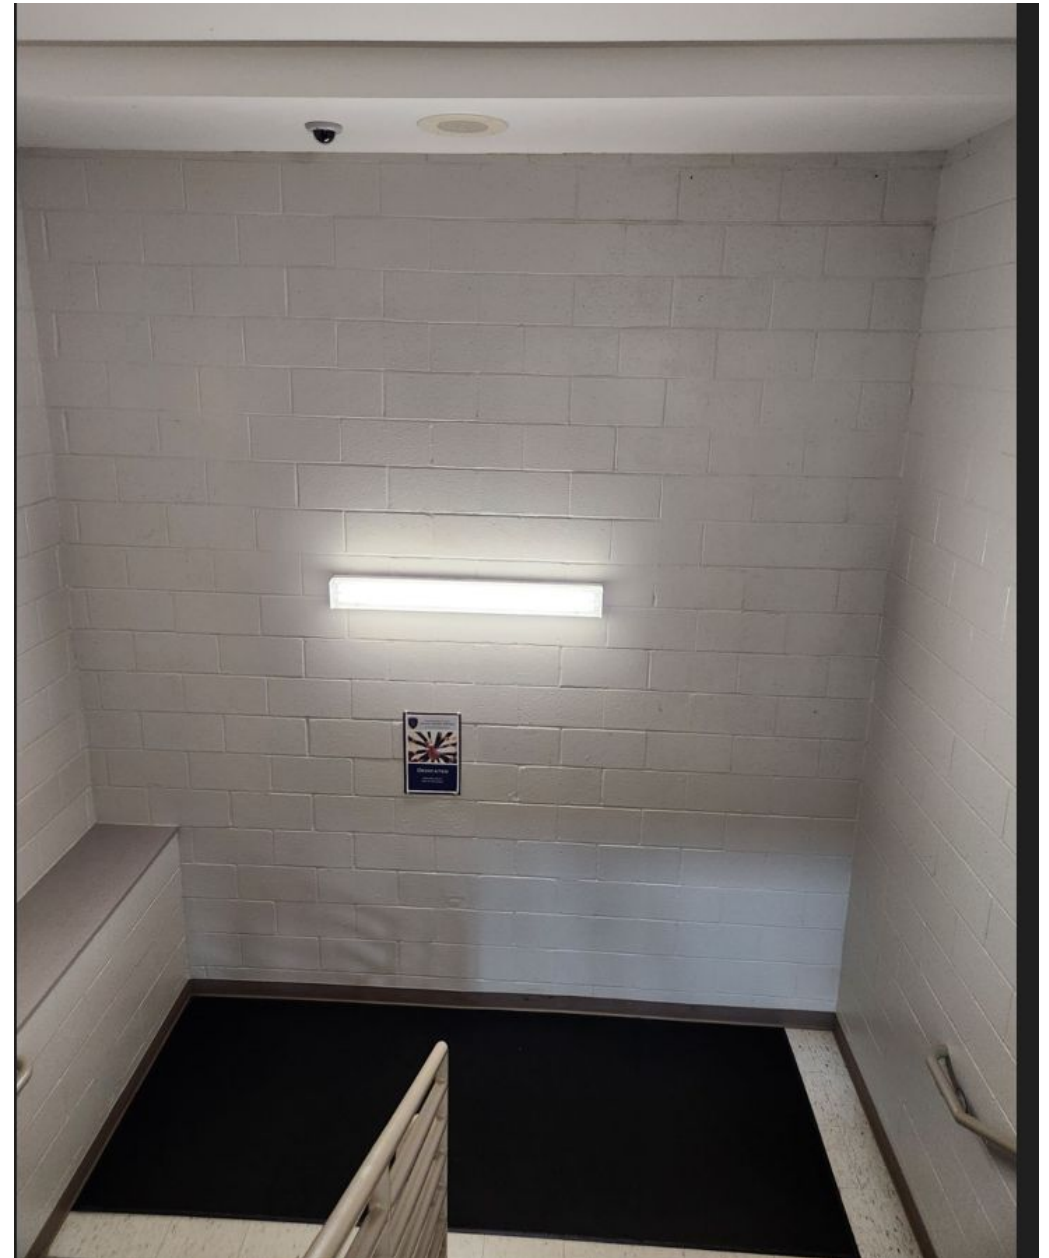

AFTER

# INTERIOR & STEM PLAQUES



Status: The project team has accepted the change proposal from the contractor. Currently waiting on production timeline.



# CAFETERIA



**Status:** Signage has been removed and the tiles are patched.  
**Essential Question** is everyone ok with putting Chautauqua Lake where it said Thunderbird Cafe?



# CAFETERIA



**Status: Signage has been removed and the tiles are replaced.**

**Group Consensus: Remove and replace tiles; possibly use new logo in the future if cost/time permits**




# LARGE GROUP INSTRUCTION ROOM



**Status: The logo will be removed and the wall panels will be replaced with light grey to match. The lead times for these panels are 6-8 weeks.**

# GYMNASIUM SCOREBOARD

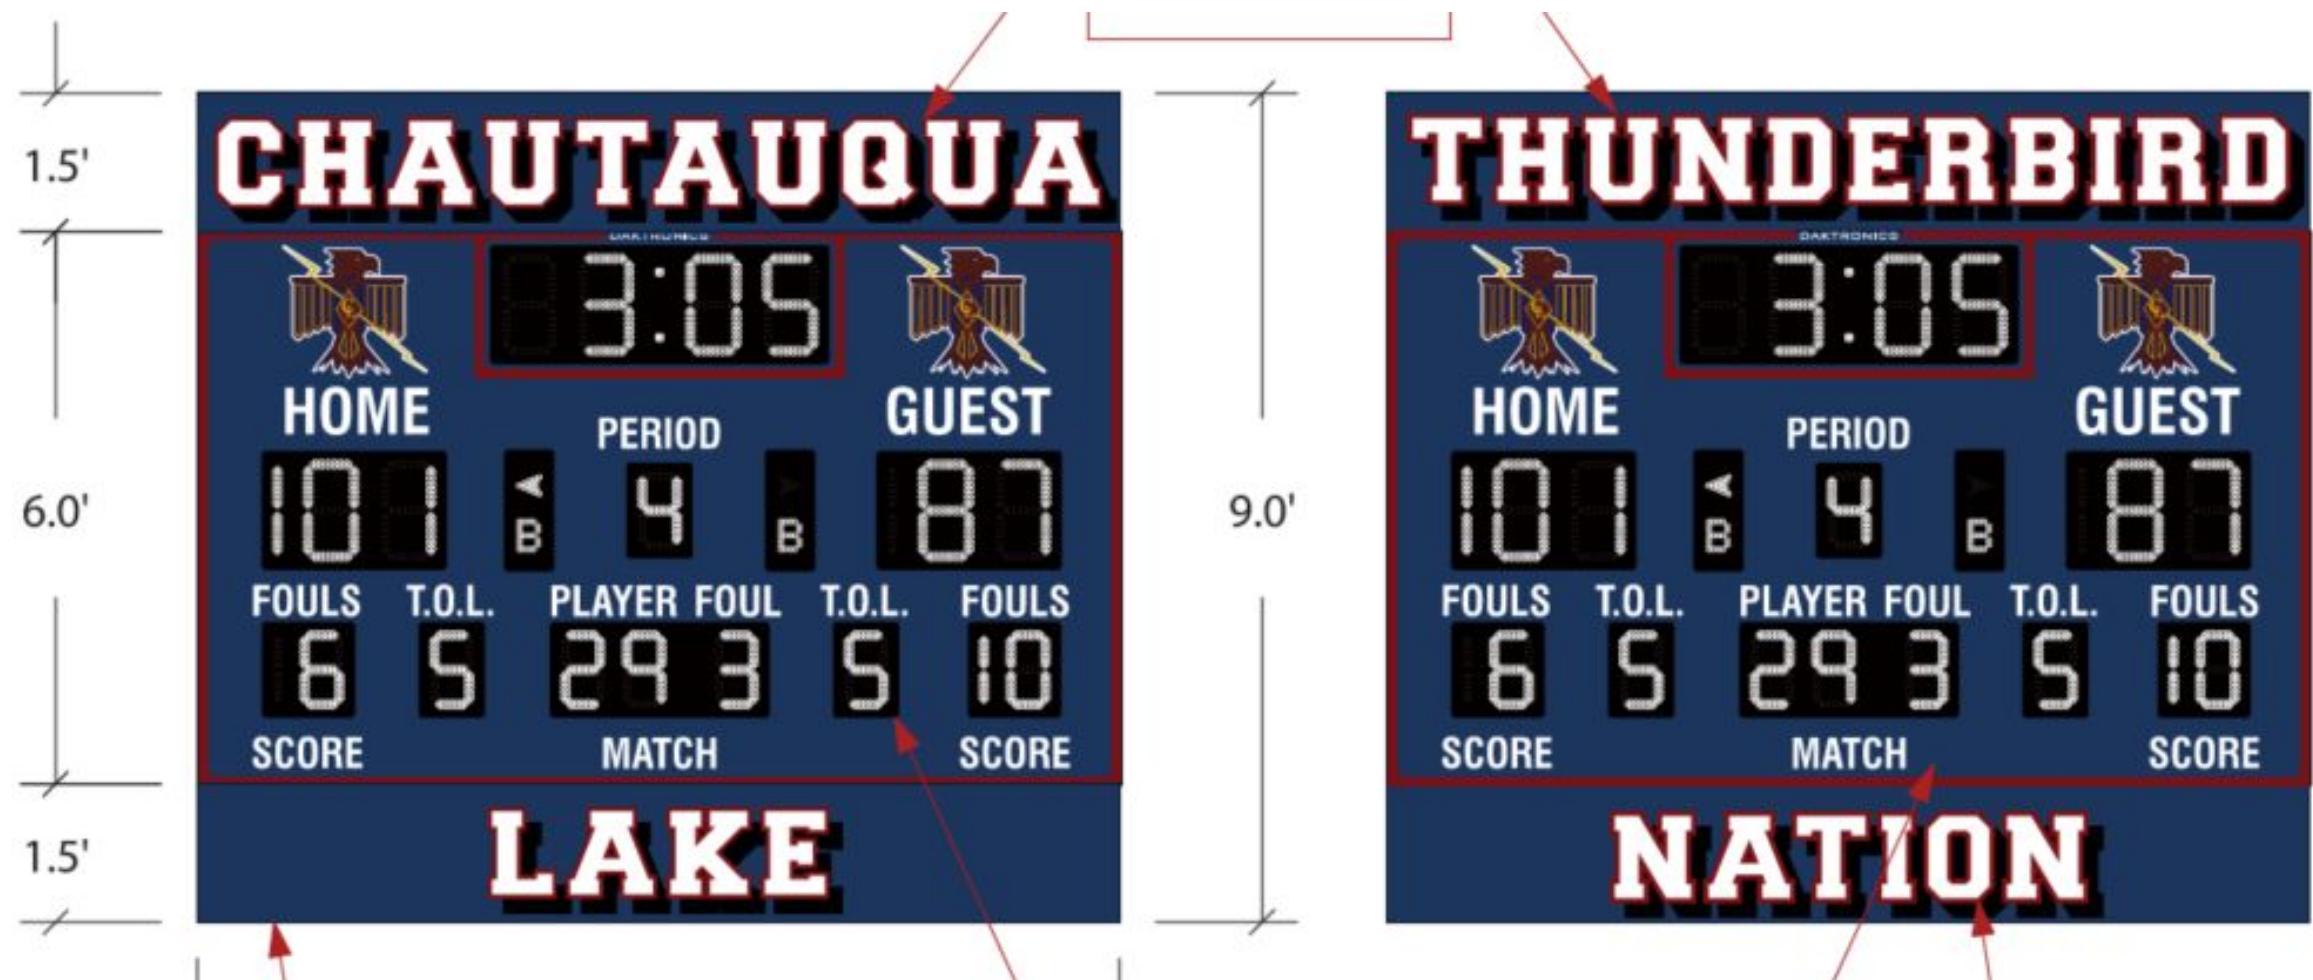

Status: The new scoreboards will both have “CHAUTAUQUA LAKE” on the top and bottom panels. The logo above the scores will be removed and replaced with a blank navy panel. The project team has approved this change proposal and will be scheduled with the contractor.



## Expedited Timeline (see attachment):

The following is the timeline for the transition plan:

### June-August 2023:

- CL Leadership Team will identify and select members for the CL Campus & CL Design Committees.
- CL Campus Committee will identify and create a prioritized list of areas that have the term “Thunderbird” depicted and aligned imagery.
- CL Campus Committee will work to devise strategies to remove and/or replace the “Thunderbird” name and imagery.

### September-December 2023:

- Creation of CL Design Committee.
- The Design Committee will develop strategies to gather feedback and ideas from various school community members.
- CL Design Committee will accumulate feedback from the school community, including students, parents, employees and board members to narrow down the list of possible nicknames.
- CL Design Committee will devise a method by which a new nickname will be selected.
- CL Design Committee will recommend a new nickname to the BOE no later than December 31, 2023.

### July 2023 -June, 2024

- The CL Campus Committee will use a prioritized list to begin to replace “Thunderbird” imagery and nickname by June 30, 2024.

### July 2024-June, 2025

- Remove any remaining “Thunderbird” graphics and imagery and/or replace it with the new nickname by June 30, 2025.



# Questions & Comments

## Next Meeting: September
